



## NATIONAL ASSOCIATION OF POSTAL SUPERVISORS

*National Headquarters*  
1727 KING STREET, SUITE 400  
ALEXANDRIA, VA 22314-2753  
(703) 836-9660

January 31, 2025

### **Board Memo 014-2025: Latest RPDC Presentation**

#### **Executive Board,**

NAPS HQ has received from the USPS the latest update on RPDC sites under construction in accordance with the DFA plan.

Thank you and be safe.

NAPS Headquarters

**Jim Herrmann:  
Sr. Director, Network  
Transformation  
01/23/25**

## RPDC Update

### Indianapolis:

- Completed Activities:
  - Relocate MPA OG Volume to RPDC – 12/28/24
    - MPA 2 Closed
  - Relocate MPA Dest Volume to RPDC – 1/18/25
    - MPA 1 Closed
- Future Activities:
  - Additional RTH volume – 2/3/25
  - Relocate Express operation – Currently @ High School Rd Annex
  - Relocate Tray sortation – full network

## RPDC Update

### Charlotte LPC:

- Completed Activities:
  - Equipment testing / burn in
  - OG: 1/4/25
  - Power test
- Future Activities
  - New Generator – 1/31/25
  - Destinating L/F
    - Charlotte 282 – 2/8/25
    - Remaining ZIPs – 2/22/25

# RPDC Update

## Chicago:

- Completed Activities:
  - Busse closed
  - USS-XL installed
  - FRS Operational
  - Fox Valley: HOPS Installed
- Future Activities
  - South Suburban: new HOPS
    - Packages offloaded to Fox Valley starting 1/25/25 during installation
  - APBS to be relocated - RPDC
  - Install HSTS - RPDC
  - Fox Valley: install DBCSs / AFSMs

## RPDC Update

### Houston:

- Completed Activities:
  - N Houston:
    - HOPS 3 and 4 accepted effective 11/1
  - PSA Closed – 1/18/25
- Future Activities:
  - Remove APBS: North Houston
  - BMEU Upgraded – 3/12/25
  - Deploy PILS (1 North, 2 South)
  - Insource THS – 5/12/25

## RPDC Update

### Atlanta:

- Cross Dock Operation continued post PEAK
  - Allows for more RTH Volume
- Cross Dock Operation being reviewed for extended usage
  - Move to CTHO
  - Part of RPDC

## RPDC Update

### Jacksonville:

- Meeting 1/23/25
- Key topics:
  - APPS performance
  - Upgrading PSMs complete – 3/1/25
  - Packages move back from PSA
  - Letter / Flat move from LPC
  - LPC Restack plan
  - Staffing plans

# RPDC Update

## Arizona: RTH

- New Facility
- Operations
  - RTH
- Equipment
  - Initially
    - 5 SIPS
    - HSTS
    - FRS
  - Future
    - Matrix – smaller version of a MaRS
    - June 2025

# RPDC Update

## Dallas: RTH

- New Facility
- Operations
  - RTH
- Equipment
  - Initially
    - 4 SIPS
    - HSTS
    - FRS
  - Future
    - Matrix – smaller version of a MaRS
    - May 2025

## RPDC Update

### Greensboro:

- Project being redesigned
  - 70% Review: TBD
  - Increase package capacity

## RPDC Update

Portland:

- Ongoing Activities:
  - Restack:
    - Medford
    - Eugene

Done

## RPDC Update

Boise:

- Upcoming Activities:
  - Insource THS
    - Complete 08/19/24
  - Officially an RPDC: 10/1/24

Done

## RPDC Update – Projects on Hold

Santa Clarita:

Royal Palm:

Oklahoma City:

## STC Implementation Dates

- Chicago
  - Incorporate into RPDCs / RTHs
  - Phases
  - Full insourcing by 4/1/25


# RTH Initiative

- Current Hub Sites:

- Atlanta GA / Seminole (Orlando)
- NJ NDC / Philadelphia PA NDC
- Denver CO
- ~~Salt Lake City UT / San Fran NDC~~
- Memphis TN
- West Valley (Phoenix) / AZ RPDC
- Indianapolis IN
- Charlotte NC
- Dallas TX
- LA NDC
- Pennwood replace Philadelphia 12/30 - delayed
- Des Moines IA

- Potential Hubs:

- Omaha NE / Kansas City MO

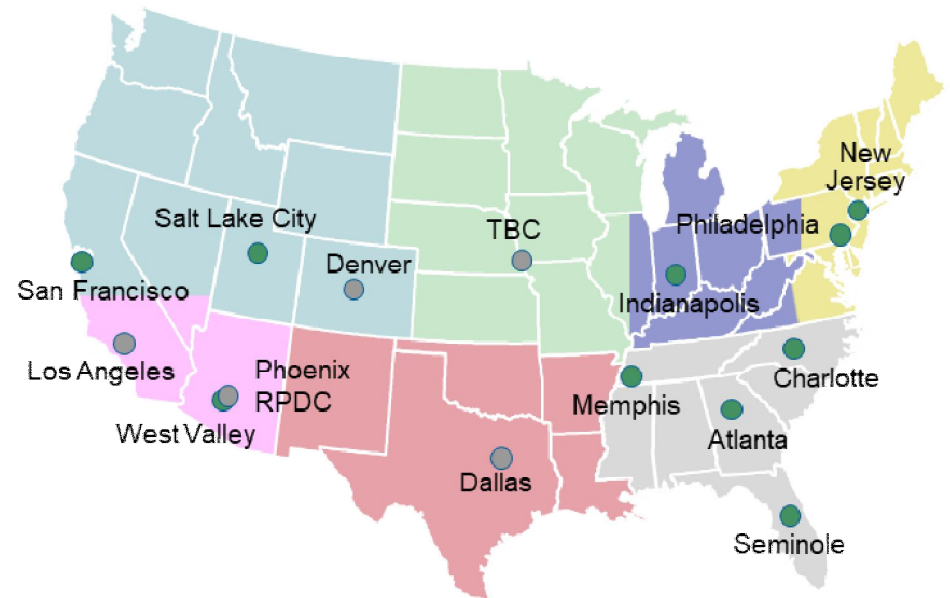

Thank you / Questions
