



NATIONAL ASSOCIATION OF POSTAL SUPERVISORS

National Headquarters
1727 KING STREET, SUITE 400
ALEXANDRIA, VA 22314-2753
(703) 836-9660

March 3, 2025

Board Memo 024-2025: Latest RPDC Presentation

Executive Board,

NAPS HQ has received from the USPS the latest update on RPDC sites under construction in accordance with the DFA plan.

Thank you and be safe.

NAPS Headquarters

**Jim Herrmann:
Sr. Director, Network
Transformation
02/20/25**

RPDC Update

Indianapolis:


- Additional RTH volume – 2/3/25
 - Nearly 100K RTH on 1/18
 - Cigna – 100K / day – started 2/10
 - Shifted Approx 200K to Chicago
- Triage operation at MPA 1 - temporary
 - MaRS (any machinable)
 - SIPS (RTH only)
 - HSTS (working trays and tubs)
 - OB Docks (cross dock containers)
 - Indy LPC: Letters and Flats
 - NMOs
- Relocate Express operation – Currently @ High School Rd Annex
- Relocate Tray sortation – full network

RPDC Update

Charlotte LPC:

- New Transformer – 2/9/25
- Transformer energized – ~~2/12~~ – Delayed due to weather
 - Date TBD
- Destinating L/F
 - Charlotte 282 – ~~2/15/25~~ – 3/1/25
 - Remaining ZIPs – ~~2/22/25~~ – 3/8/25
- Johnson City
 - 242, 246*, 379
 - Destinating Packages – Network: 2/24 to Charlotte
 - New facility - July

Johnson City LPC: Finalized OSL

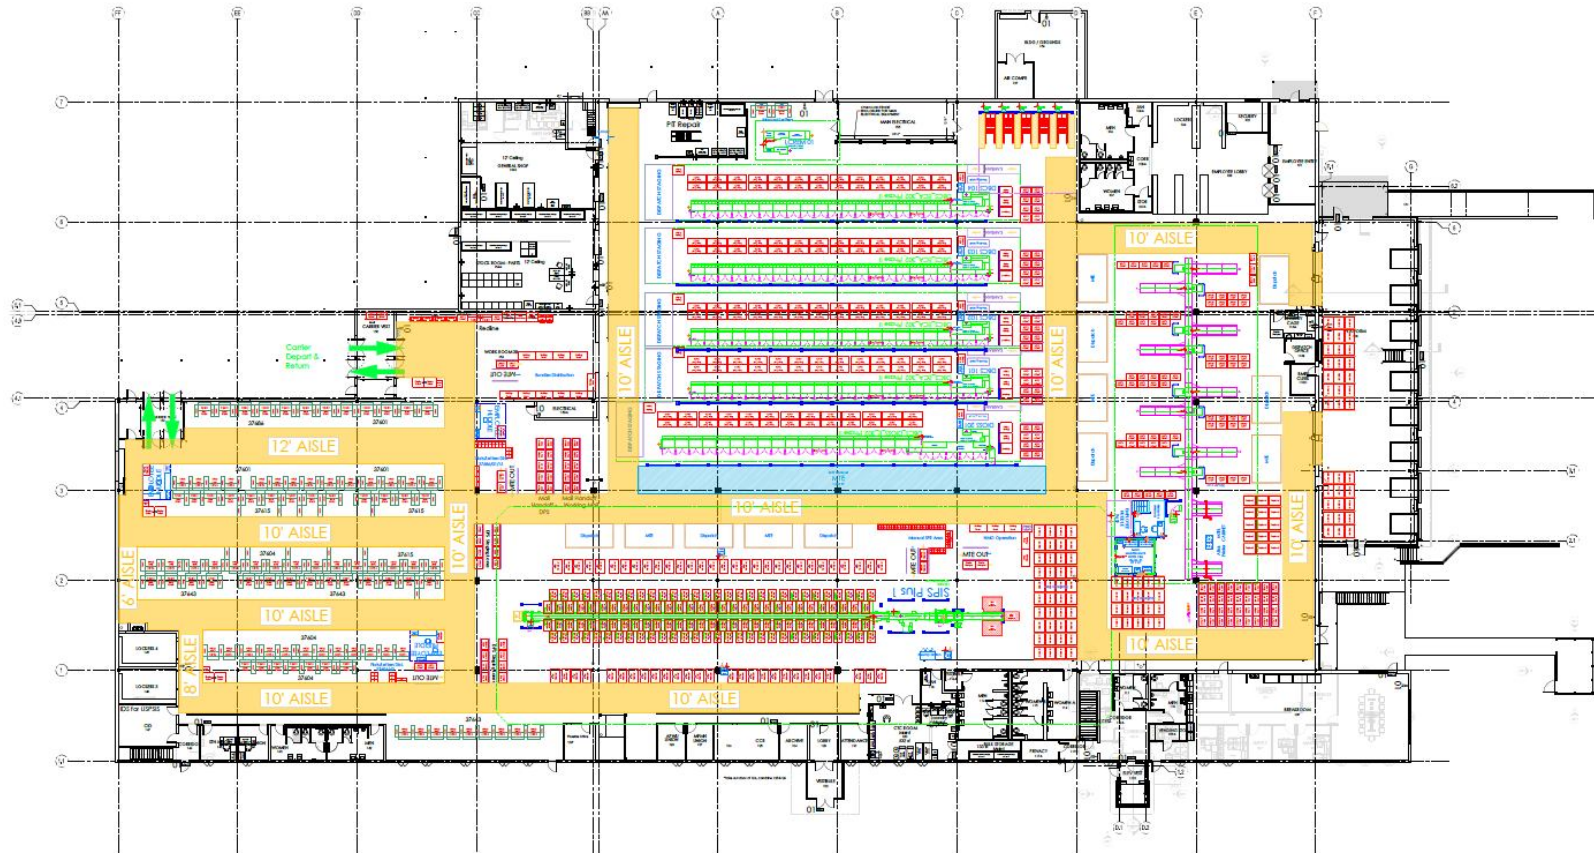

RPDC Update

Chicago:

- Completed Activities:
 - Busse closed
 - USS-XL installed
 - FRS Operational
 - Fox Valley: HOPS Installed
- Future Activities
 - South Suburban: new HOPS
 - Packages offloaded to Fox Valley starting 1/25/25 during installation
 - APBS to be relocated - RPDC
 - Install HSTS - RPDC
 - Fox Valley: install DBCSs / AFSMs

RPDC Update

Houston:

- Completed Activities:
 - N Houston:
 - HOPS 3 and 4 accepted effective 11/1
 - PSA Closed – 1/18/25
- Future Activities:
 - Remove APBS: North Houston
 - BMEU Upgraded – 3/12/25
 - Deploy PILS (1 North, 2 South) – may be delayed
 - Insource THS – 5/12/25

RPDC Update

Atlanta:

- Cross Dock Operation continued post PEAK
 - Allows for more RTH Volume
- Cross Dock Operation being reviewed for extended usage
 - Move to CTHO
 - Part of RPDC

RPDC Update

Jacksonville:

- Ongoing topics:
 - APPS performance
 - Upgrading PSMs complete – 3/1/25
 - Packages move back from PSA – 3/15
 - Letter / Flat move from LPC – 4/19
 - LPC Restack plan
 - Staffing plans
- May keep PSA for RTH processing – Destinating Florida
- Destinating package processing at Tallahassee

RPDC Update

Arizona: RTH

- New Facility
- Operations
 - RTH
- Equipment
 - Initially
 - 5 SIPS
 - HSTS
 - FRS
 - Future
 - Matrix – smaller version of a MaRS - **MEWS**
 - June 2025

RPDC Update

Dallas: RTH

- New Facility
- Operations
 - RTH
- Equipment
 - Initially
 - 4 SIPS
 - HSTS
 - FRS
 - Future
 - Matrix – smaller version of a MaRS - **MIMS**
 - **Acceptance: May 2025**
 - **Operational: June 2025**

RPDC Update

Kansas: RTH

- New Facility – Gardner KS
- Operations
 - RTH
- Equipment
 - Initially
 - 6 SIPS
 - HSTS
 - FRS / USS XL
 - Future
 - Phase 2 - TBD

RPDC Update

Greensboro:

- Project being redesigned
 - 70% Review: TBD
 - Increase package capacity

RPDC Update

Portland:

- Ongoing Activities:
 - Restack:
 - Medford
 - Eugene

Done

RPDC Update

Boise:

- Upcoming Activities:
 - Insource THS
 - Complete 08/19/24
 - Officially an RPDC: 10/1/24

Done

RPDC Update – Projects on Hold

Santa Clarita:

Royal Palm:


Oklahoma City:

STC Implementation Dates

- Chicago
 - Incorporate into RPDCs / RTHs
 - Phases
 - Full insourcing by 4/1/25

RTH Initiative

- Current Hub Sites:
 - Atlanta GA / Seminole (Orlando)
 - NJ NDC / Philadelphia PA NDC
 - **Denver CO**
 - ~~Salt Lake City UT~~ / San Fran NDC
 - Memphis TN
 - West Valley (Phoenix) / **AZ RPDC**
 - Indianapolis IN
 - Charlotte NC
 - **Dallas TX**
 - LA NDC
 - Pennwood replace Philadelphia 12/30 - delayed
 - Des Moines IA
- Potential Hubs:
 - Omaha NE / **Kansas City MO**

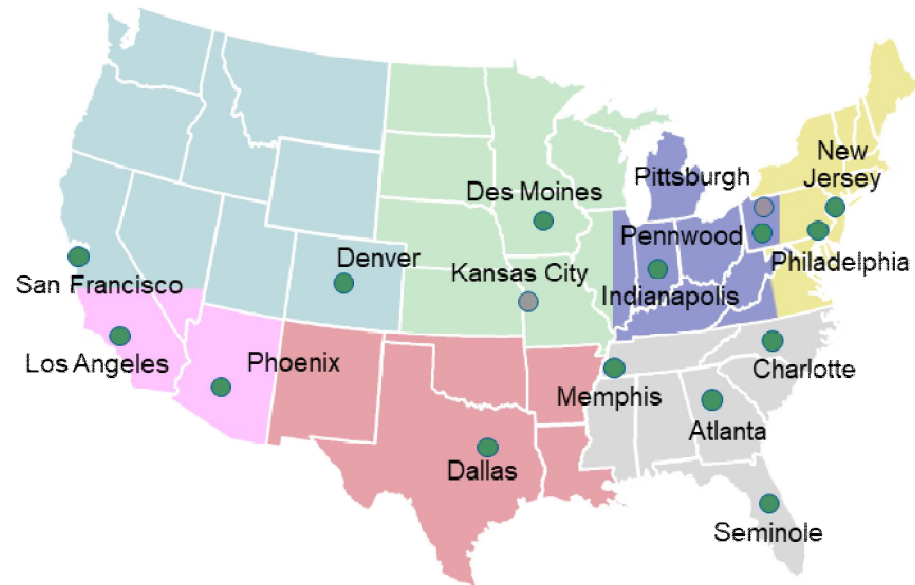

Thank you / Questions
