



NATIONAL ASSOCIATION OF POSTAL SUPERVISORS

National Headquarters
1727 KING STREET, SUITE 400
ALEXANDRIA, VA 22314-2753
(703) 836-9660

March 2, 2026

Board Memo 011-2026: Latest RPDC Presentation

Executive Board,

NAPS HQ has received from the USPS the latest update on RPDC sites under construction in accordance with the DFA plan.

Thank you and be safe.

NAPS Headquarters

Network Updates

02/26/2026

RPDC activation status definitions

Status	Definition
Initial state	They have not yet updated their mail and package flow to future-state and are in design or initial fit-out phase.
Partially active	They have adopted a new layout, but are not processing all future-state products and/or ZIP Codes. The main package sorter(s) are running at partial capacity.
Significantly active	They are processing majority of future-state products and/or ZIP Codes with the main package sorter(s) at full operations.
Regional Transfer Hub active	They are processing network volume, enabling origins to reduce the number of separations and send mail and packages to a single consolidation point versus many destinating plants. The RTH then sorts and distributes to destinating plants in their region.

New RPDC Projects

- Dallas
 - Campus Review
- Denver
 - Denver PDC -> Denver RPDC
 - Denver NDC -> Denver RTH (Northwest)
- Los Angeles
 - Campus Review
- Fargo
- Puerto Rico


Denver RPDC

Denver RPDC

- Outgoing and Destinating Packages
- Remove existing package equipment
- Install 5 PILS
 - 7/16
 - 7/16
 - 9/3
 - 9/3
 - 9/10


Denver- Current OSL

CURRENT MACHINE SETS		
MACH TYPE	COUNT	BIN NBR
DBCS	29	270
DBCS	1	254
DBCS	1	238
DBCS	9	222
DIOS	5	222
LCTS	4	N/A
AFSM	3	N/A
AFCS	8	N/A
LCREM	1	N/A
HTPS	1	388
HDUS	1	107
SPSS	1	196
SIPS+	2	200

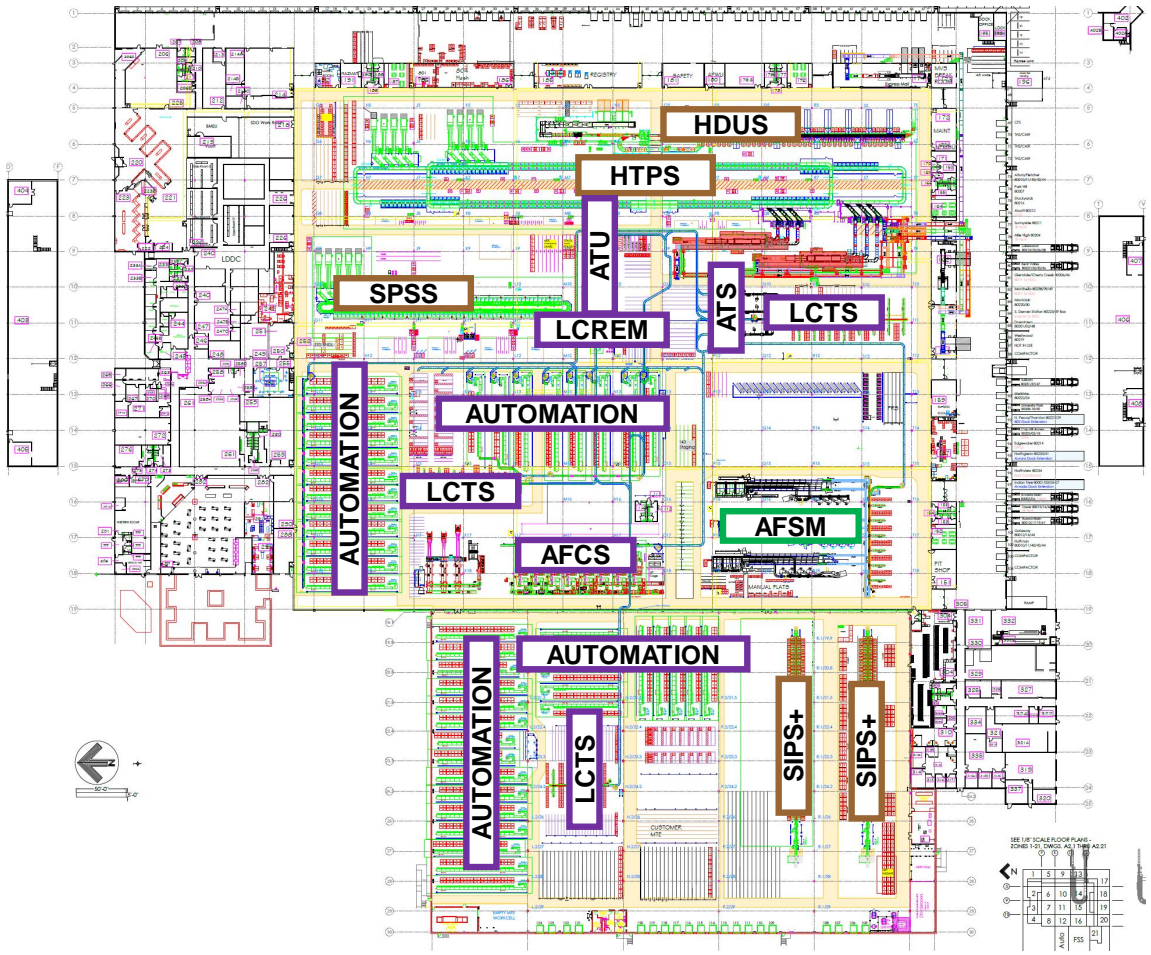

Denver- Future OSL

CURRENT MACHINE SETS		
MACH TYPE	COUNT	BIN NBR
DBCS	20	302
DBCS	11	270
DBCS	1	254
DBCS	1	238
DIOSS	4	270
HSTS	1	N/A
AFSM	3	N/A
AFCS	5	N/A
LCREM	1	N/A
PILS	5	200
HDUS	1	107

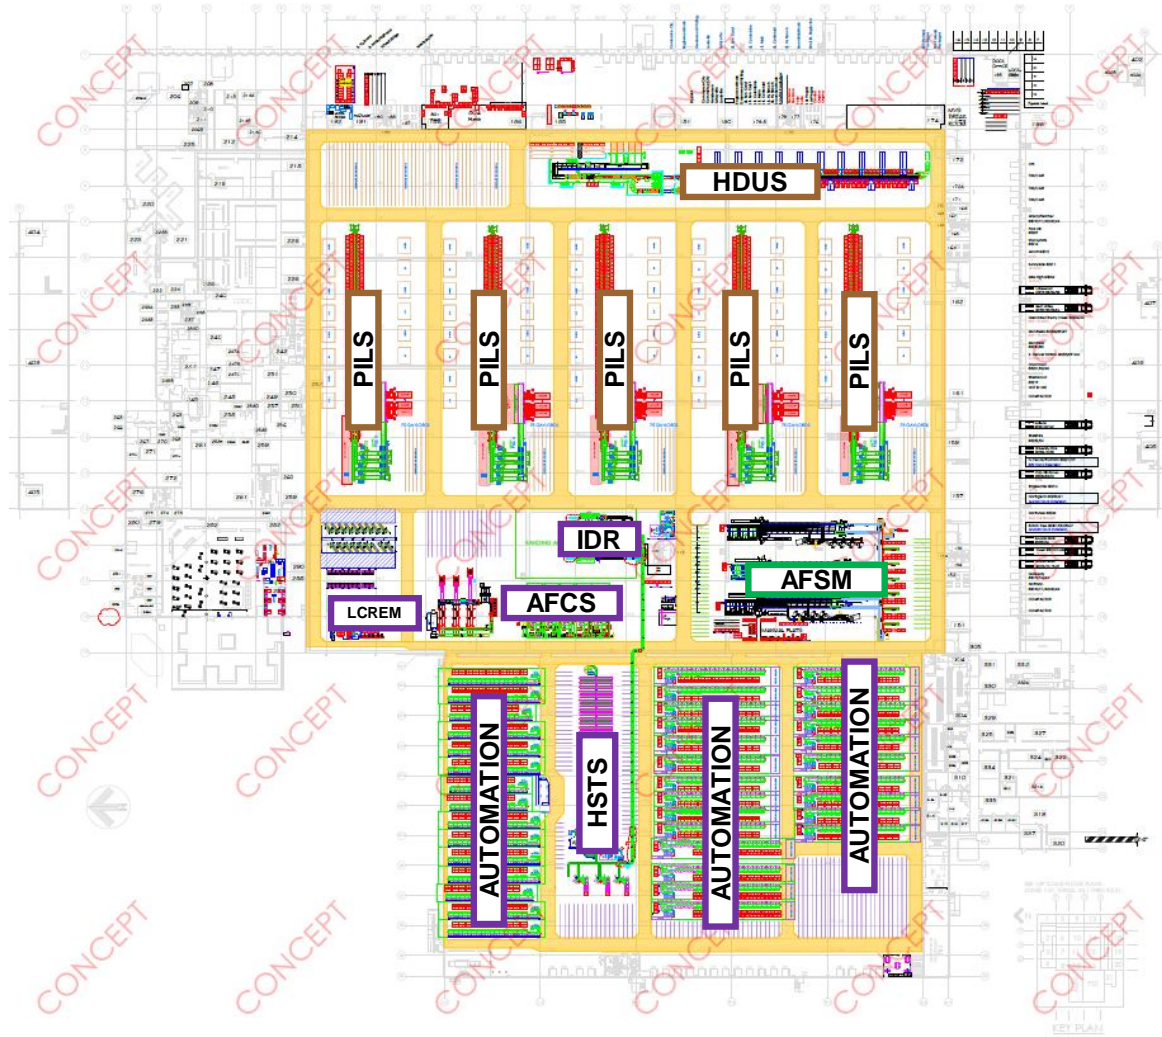

Denver RTH Insourcing

Denver RTH - Insourcing


- ❑ Insourced by 2/23
 - ❑ 3 phases: 2/09, 2/16, 2/23
- ❑ 3 Locations
 - ❑ Denver NDC:
 - ❑ 88K
 - ❑ Salt Lake City PDC
 - ❑ 61K
 - ❑ San Francisco NDC
 - ❑ 112K
- ❑ Relocated 3 SIPS+ (48 bin) from AZ

Memphis TN RPDC

Memphis TN RPDC - Notes

- Finalize volume to be ran at the RPDC in Phase 1 (Peak)
 - RTH
 - 20K: TBD
 - OG from MPA: 5/16
 - OG from Little Rock: 5/30
- Equipment Schedules
 - PILS 1: 11/21
 - PILS 2: 11/28
 - USS XL: 11/18
 - PILS 3: 4/16
 - PILS 4: 4/30
 - Matrix Sorter - TBD


Memphis TN RPDC – Phase 1 (11/03/25)

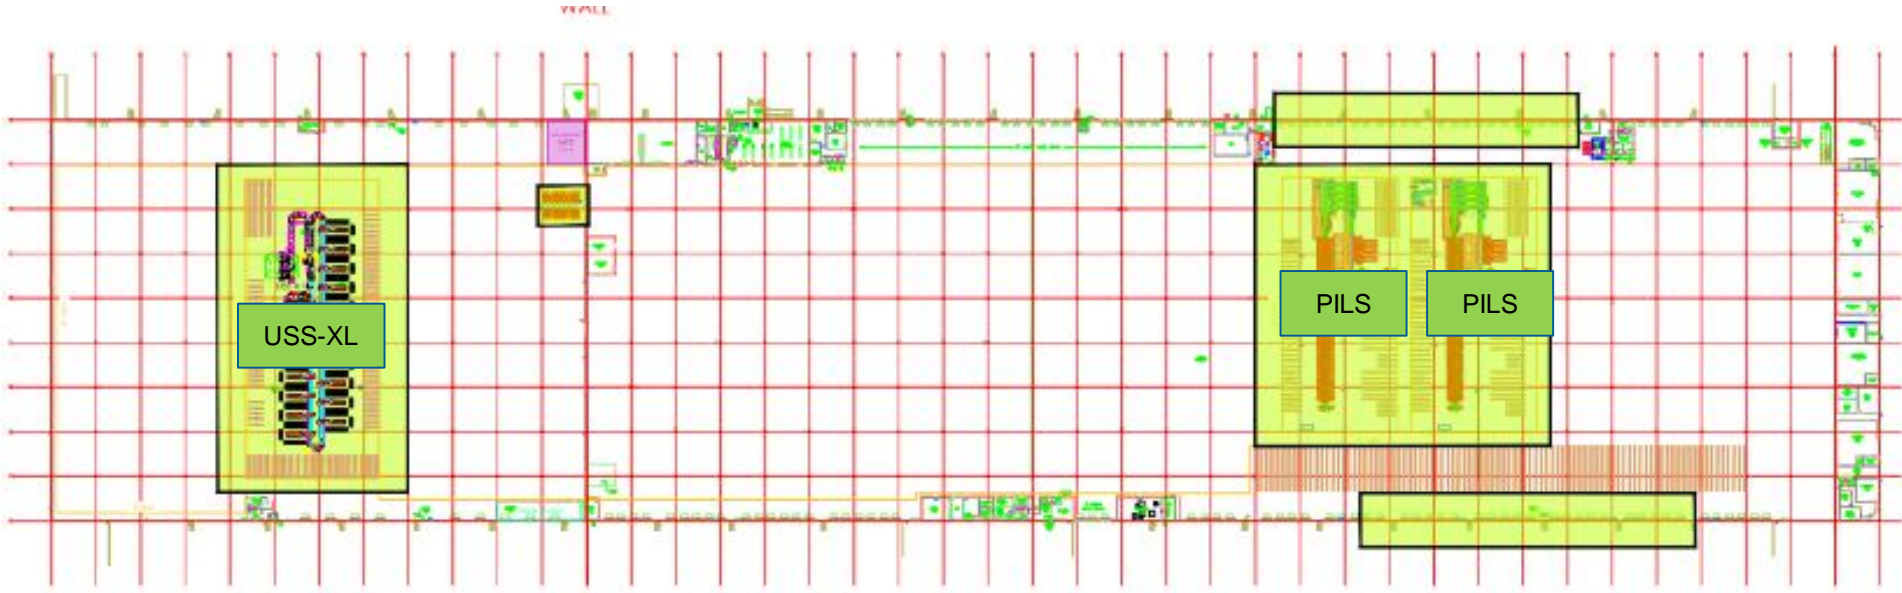

Phase Timeline
Phase 1 (11/03/2025)
Phase 2 (03/01/2026)
Phase 3 (06/30/2026)

Phase 1 Equipment Set	Target Completion Date
2 PILS (200 Bins)	
1 USS XL (18 Legs)	

Memphis TN RPDC – Phase 2 (03/01/2026)

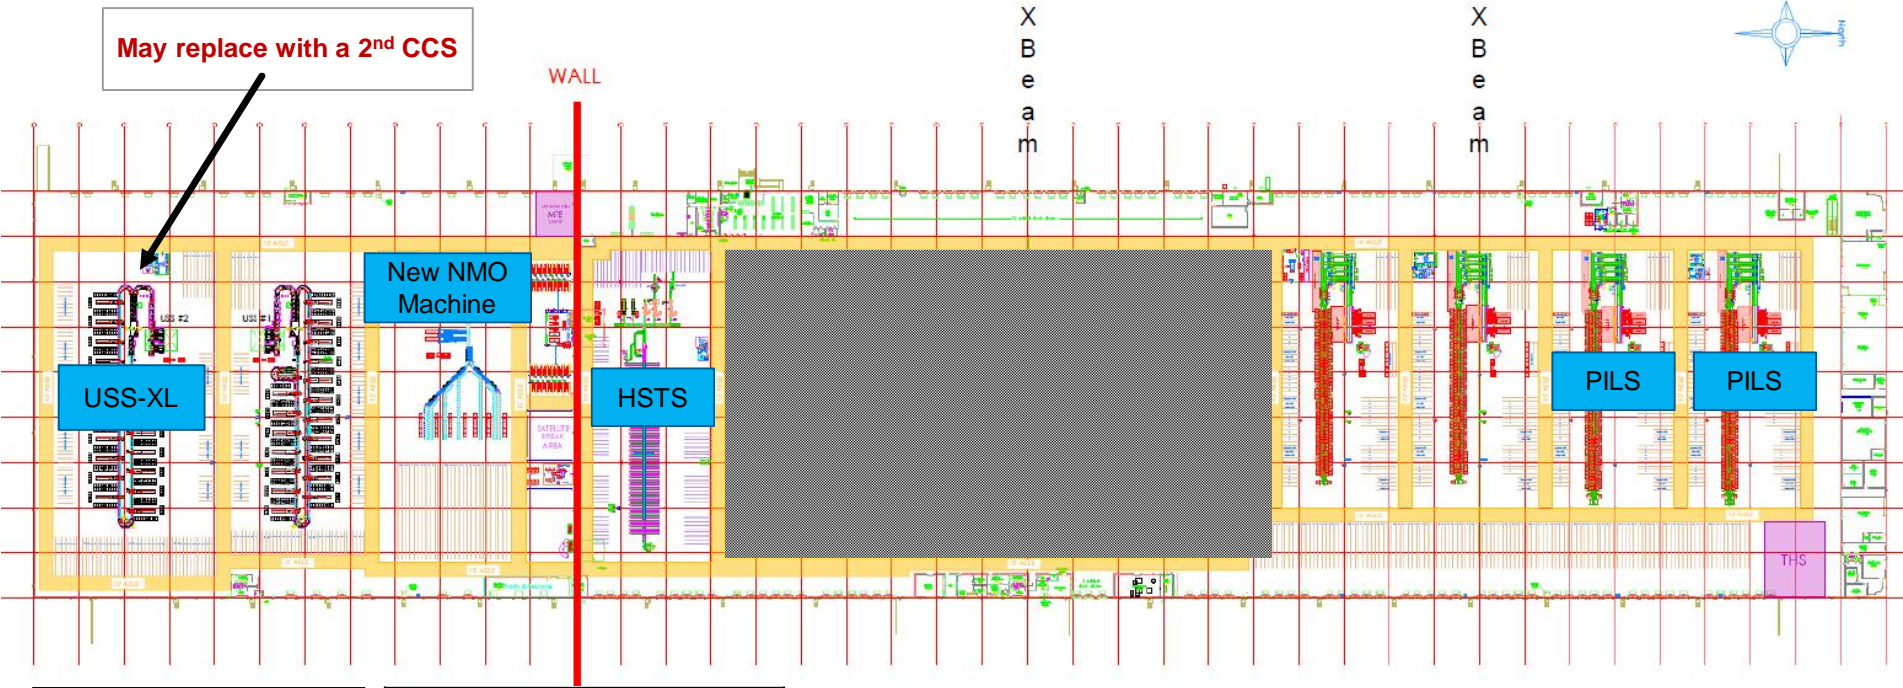

Phase Timeline
Phase 1 (11/03/2025)
Phase 2 (03/01/2026)
Phase 3 (06/30/2026)


Phase 2 Equipment Set
2 PILS (200 Bins)
1 USS XL (18 Legs)
New NMO Machine
HSTS (92 Legs)

St. Louis PSA

St. Louis PSA – Notes

- PSA Equipment Schedule
 - HSTS: TBD
 - SIPS+: TBD
 - RTH
 - 01/12/2026:
 - 67K
 - TBD:
 - 110K (Total of 170K)
- St Louis Annex
 - 12/26/2025: Closed
- St Louis NDC
 - Replace APBS with 2 SIPS+
 - Dates:
 - 2/12/26
 - 3/19/26


St Louis PSA – Phase 1 Layout

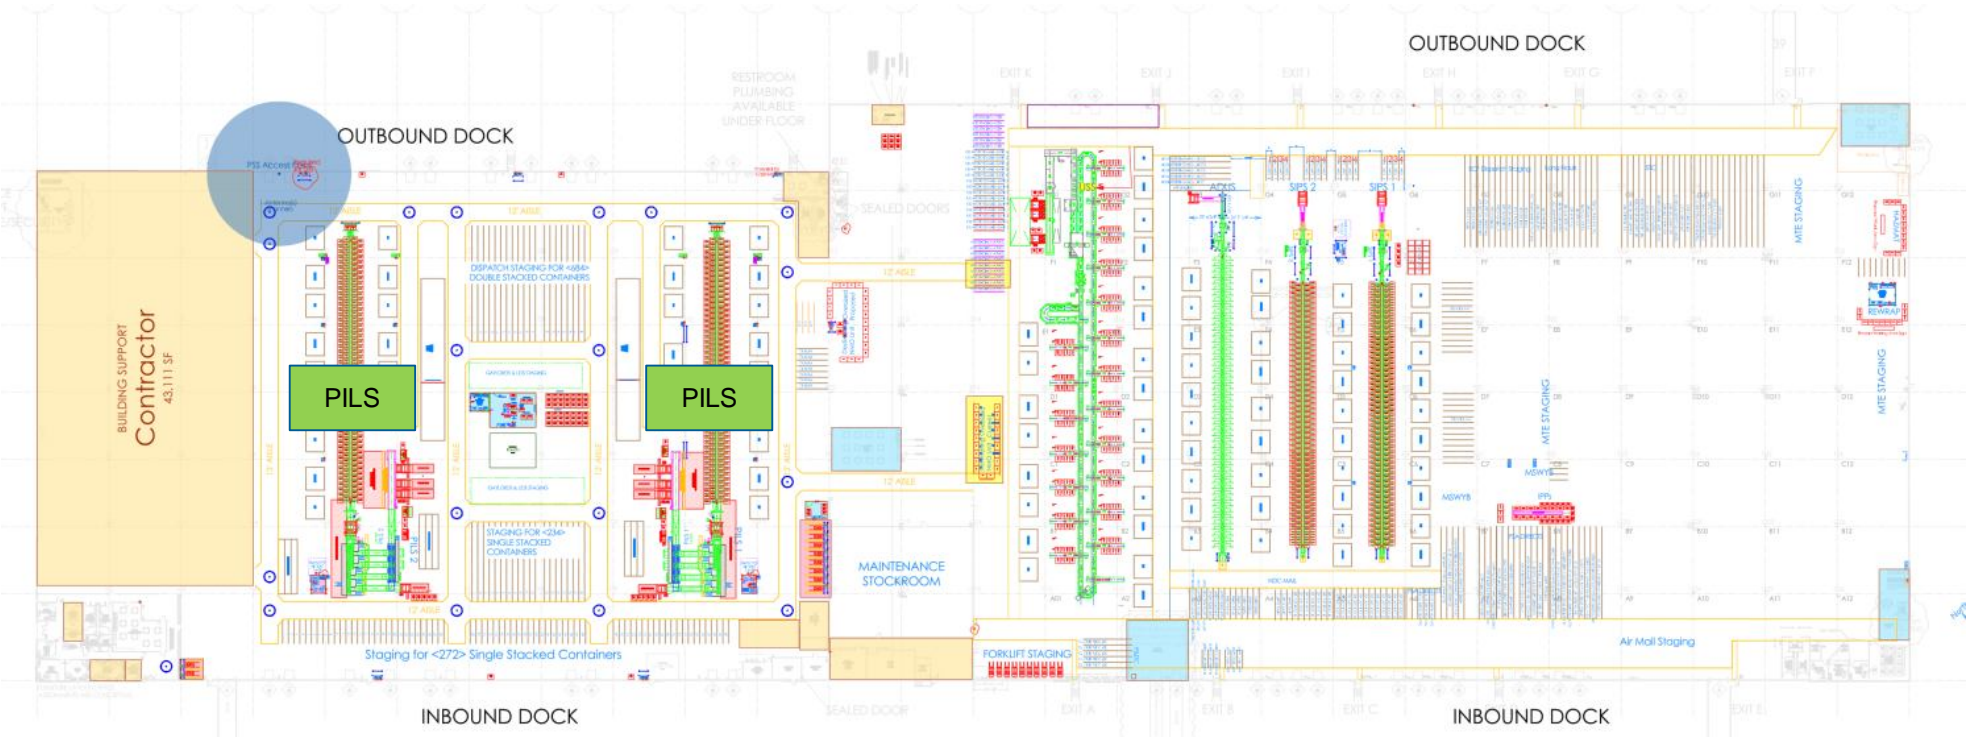

Phase Timeline
Phase 1 (8/4/2025-10/22/2025)
Phase 2 (2/19/2026-7/13/2026)

Phase 1 Equipment Set	Target Completion Date
2 PILS	10/22/2025

St Louis PSA – Phase 2 Layout

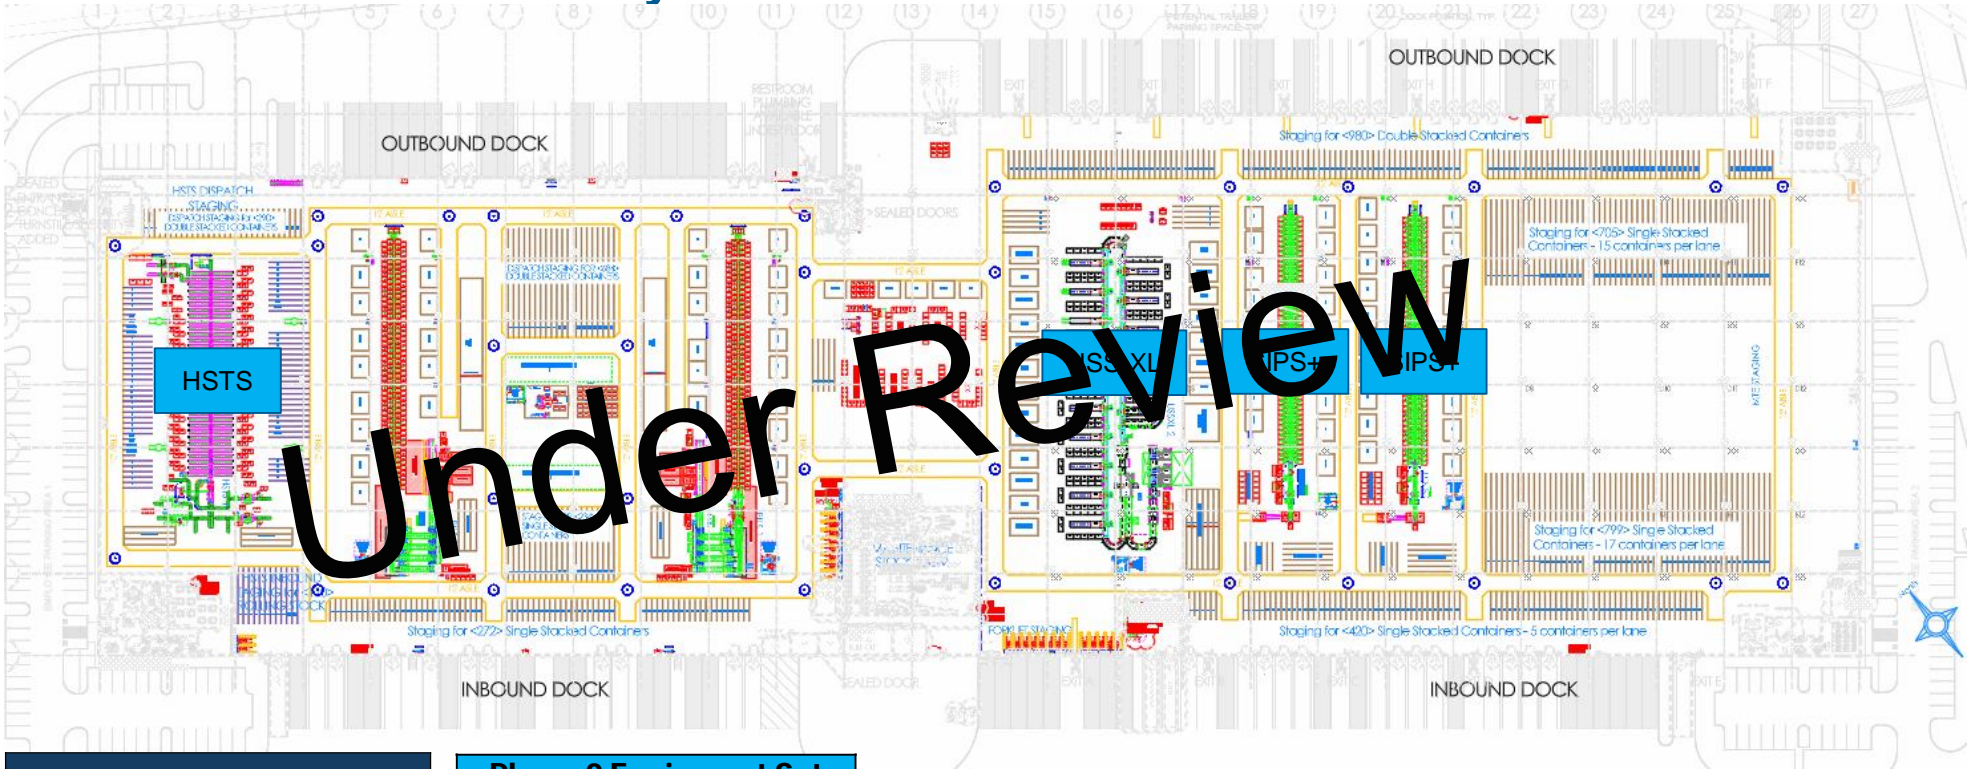

Phase Timeline
Phase 1 (8/4/2025-10/22/2025)
Phase 2 (2/19/2026-7/13/2026)

Phase 2 Equipment Set
2 SIPS+
1 USS-XL
HSTS


Birmingham AL RPDC

Birmingham RPDC - Notes

- Equipment Schedules
 - SIPS+ relocated from PSA: 11/22
 - PILS 1: 11/28
 - PILS 2: 7/9
 - PILS 3: 7/9

- OG sortation for PEAK: 11/28

Birmingham RPDC – Final State Layout

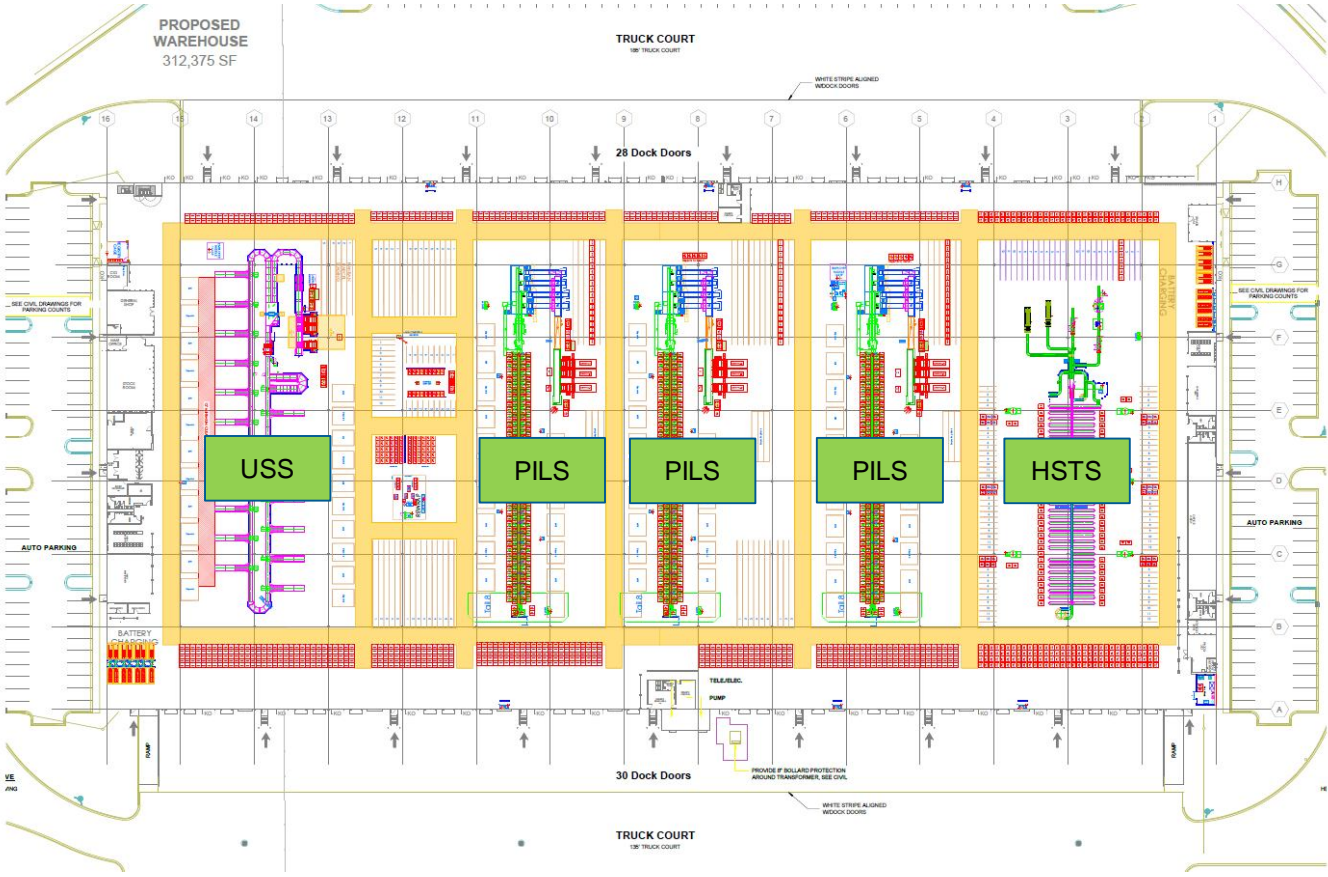

Future Equipment Set
PILS (3)
USS
HSTS

New Jersey RPDC

New Jersey RPDC - Notes

- ❑ 12/01: 6 Strands on MaRS
 - ❑ 400K capacity thru PEAK
 - ❑ 600K capacity on Sundays
 - ❑ RTH
 - ❑ 01/12/2026:
 - ❑ None planned
- ❑ 11/01: Relocate OG STC and OG NMO operations
 - ❑ Create space for D2M and child SIPS
 - ❑ New Jersey NDC Annex (old Greater Newark Facility)
 - ❑ Approx thru July 2026
- ❑ Finalize Metro Plan
- ❑ International part of Building - OSL
- ❑ Pennwood offload

Greensboro RPDC

Greensboro RPDC - Notes

- ❑ RTH volume
 - ❑ 01/12/2026:
 - ❑ 132K
 - ❑ X Dock containers – 2,500
 - ❑ Mitigation
 - ❑ TBD:
 - ❑ 160K (Total of 292K)
- ❑ APBS removal post PEAK
- ❑ Annex
 - ❑ CCS (2): 12/01 – 12/15
 - ❑ RTH NMOs
- ❑ THS Insourcing June 2026

Kansas City RTH

Kansas City RTH - Notes

- Continuing to hire
- Adjust workload when staffing supports
- 11/15: Relocate the STC from the St. Louis NDC to the Kansas RTH
- Increase RTH volume
 - 01/12/2026:
 - 116K
 - TBD:
 - 110K (Total of 340K)

Dallas RTH

Dallas RTH - Notes

☐ Increase RTH volume

☐ Jan 12:

☐ +36K – (Total of 582K)

Miscellaneous

Other Plants - Notes

- ❑ Indianapolis
 - ❑ MPA #1
 - ❑ Cross Dock Operation – indefinite
 - ❑ APPS thru PEAK ONLY

- ❑ Oak Creek – Milwaukee
 - ❑ THS Insourcing **May 2026**

- ❑ Facilities that will no longer process RTH effective Jan 12:
 - ❑ Des Moines
 - ❑ Atlanta
 - ❑ Charlotte

Jacksonville RPDC

Jacksonville RPDC - Notes

- Insourcing FL STC
 - 09/22: Phase 1
 - 09/29: Phase 2
 - 10/06: Phase 3
 - Complete
- PSA for Tallahassee offload
 - 02/26

Appendix

DFA Acronyms

- ❑ **RPDC:** Regional Processing & Distribution Center
- ❑ **LPC:** Local Processing Center
- ❑ **PSA:** Package Support Annex
- ❑ **MaRS:** Matrix Regional Sorter
- ❑ **SIPS:** Single Induction Package Sorter
- ❑ **MEWS:** Matrix East West Sorter
- ❑ **MIMS:** Multiple Induct Matrix Sorter
- ❑ **HOPS:** High Output Package Sorter
- ❑ **CHOPS:** Chained HOPS
- ❑ **D2M:** Dock To Machine
- ❑ **PILS:** Parallel Induction Linear Sorter
- ❑ **USS XL:** Universal Sort System handles larger packages
- ❑ **FRS:** Flex Rover Sorter
- ❑ **RTO:** Regional Transportation Optimization
- ❑ **CCS:** Cascading Conveyor System (NMOs)
- ❑ **ePSM:** Enhanced Package Sorting Machine
- ❑ **LCUS:** Low-Cost Universal Sorter: NMOs, trays, tubs
- ❑ **LCTS:** Low-Cost Tray Sorter
- ❑ **HSTS:** High Speed Tray Sorter
- ❑ **RTH:** Regional Transfer Hub (Go East / Go West)
- ❑ **OTH:** Origin Transfer Hub
- ❑ **OPF:** Origin Processing Facility
- ❑ **NDLL:** National Distribution Labeling List
- ❑ **ADC:** Area Distribution Center
- ❑ **AADC:** Automated Area Distribution Center
- ❑ **OMX:** Origin Mixed ADC
- ❑ **MXD:** Mixed ADC
- ❑ **DNDC:** Destination Network Distribution Center
- ❑ **DSCF:** Destination Sectional Center Facility
- ❑ **CUS:** Compact Universal Sorter
- ❑ **VRS:** Video Relabeling System

Chicago RPDC

Chicago RPDC - Notes

- APPS being upgraded
 - 11/01: 100% operational
- Power Upgrade: 11/01

- South Suburban
 - 9/15: 5 DIOSS/DBCS removals
 - 10/01: FRS being installed

Phoenix RTH

Phoenix RTH - Notes

- MEWS operational
- Increase RTH volume
 - Jan 12:
 - +133K (Total of 505K)

Charlotte RPDC

Charlotte RPDC - Notes

- ❑ Johnson City
 - ❑ 09/06: Operational
