



NATIONAL ASSOCIATION OF POSTAL SUPERVISORS

National Headquarters
1727 KING STREET, SUITE 400
ALEXANDRIA, VA 22314-2753
(703) 836-9660

May 23, 2025

Board Memo 037-2025: Latest RPDC Presentation

Executive Board,

NAPS HQ has received from the USPS the latest update on RPDC sites under construction in accordance with the DFA plan.

Thank you and be safe.

NAPS Headquarters

Union Deck


Jim Herrmann

Sr. Director, Network Transformation

05/22/25

Indianapolis IN RPDC Update:

- Triage operation at MPA 2 –
 - Relocation started 5/17/25
 - Football field
- High Density Cross-Dock operation at MPA 2
 - Limited to origins that has no Indy volume
 - Reduced origins by 6
 - Move to MPA 1 - TBD
- Relocate Express operation – Currently @ High School Rd Annex - **TBD**
- Relocate Tray sortation – full network - **TBD**

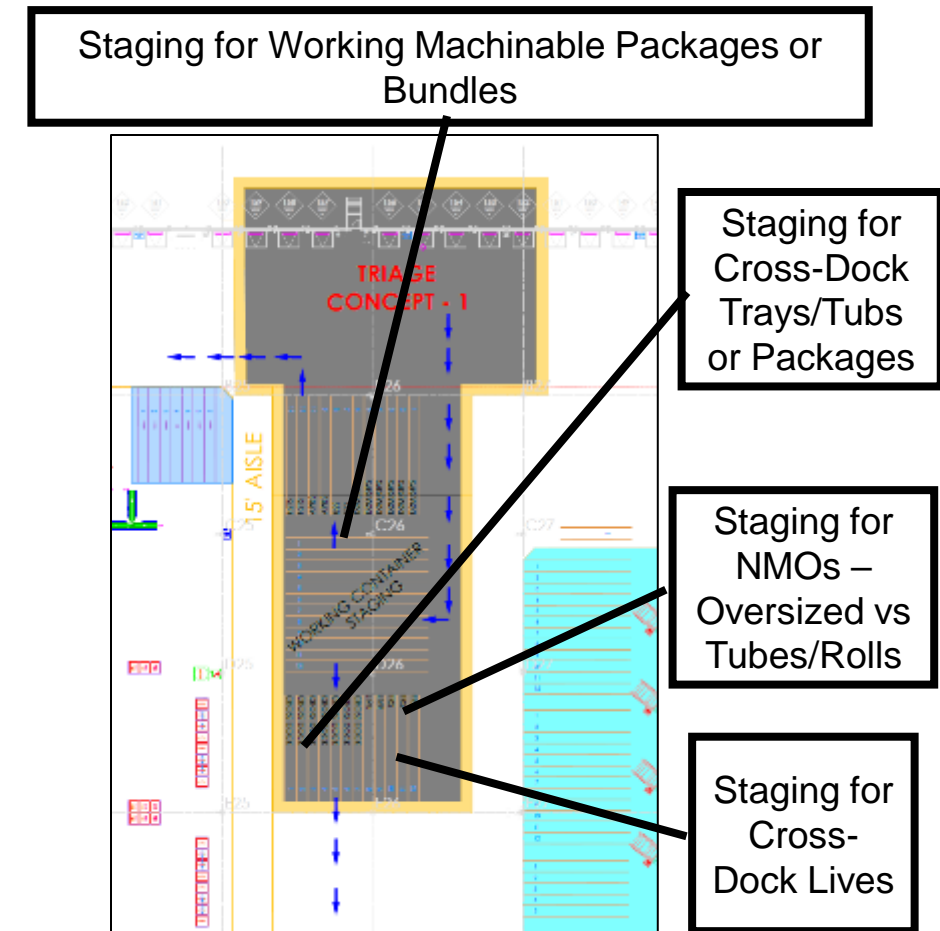

Chicago IL RPDC Update:

- Future Activities
 - South Suburban: new HOPS
 - Packages offloaded to Fox Valley starting 1/25/25 during installation
 - 7/15/25 target completion date
 - APBS relocated – 4/20/25
 - Install HSTS – RPDC – 7/08/25
 - Power upgrade – Nov 2025
 - APPS
 - Surge Conveyors
 - THS Insourcing split in two. Tentative start Date – 8/11/25
 - Chicago RPDC – Build
 - Relocate SIPS 2
 - No LCUS
 - Adjust ball decking – safety
 - Chicago ISC - Break
 - Fox Valley: install DBCSs / DIOSS – 8/4/25

Charlotte NC LPC RPDC Update:

- Destinating L/F
 - Hickory 286 – TBD (August)
 - Pending DBCS rewiring
- Johnson City
 - 242, 246*, 379
 - Destinating Packages
 - New facility – July

Houston TX RPDC Update:

- Insource THS – 5/12/25

Atlanta GA RPDC Update:

- Modification to MaRS – 5/5/25
 - Allows for keying
 - Less rejects to the floor
 - Redirect 300K of packages for 5 weeks
 - Greensboro
 - Jacksonville
 - Charlotte
 - Completed modifications to Strands 1 & 2
 - Started upgrades to strands 3 & 4

Jacksonville FL RPDC Update:

- Ongoing topics:
 - Equipment performance
 - Continue to utilize Annex
 - Letter / Flat move from LPC – 6/14/25
 - LPC Restack plan
 - Staffing plans
- PSA for RTH processing – Destinating Florida – 6/28/25
- Destinating package processing at Tallahassee

Arizona RPDC Update:

- Future
 - Permanent power delayed: 7/31/25
 - MEWS
 - Using 2 Generators for acceptance
 - Acceptance testing: in process
 - Operational: 6/21/25

Dallas TX RPDC Update:

- New Facility
- Operations
 - RTH
- Equipment
 - Initially
 - 4 SIPS
 - HSTS – 6/2/25
 - Remove LCTS
 - FRS – upgrade to 4 inducts – 5/19/25
 - Future
 - 60K RTH – 5/19/25
 - MIMS – 6/5/25
 - Critical Date: Power upgrade: 4/8/25 complete

Kansas City MO RPDC Update:

- New Facility – Gardner KS
- Operations
 - RTH – 45K (machinable packages only working)
 - High Density Cross Dock
 - Equipment
 - 6 SIPS
 - HSTS
 - FRS
 - **USS XL – 7/30/25**
 - Staffing – **Challenge**
 - Future
 - **Phase 2 – 5/27/25**
 - Working RTH volume - 45K
 - Trays – 2K
 - NMOs

Greensboro NC RPDC Update:

- Project being redesigned
 - 70% Review: **5/08/25**
 - Increase package capacity
 - **Limited Operations by PEAK**

New Jersey RPDC Update:

- MaRS
 - Stakeholder kick-off meeting **05/19/25**
 - Limited operations by PEAK

Misc RPDC Update:

- Denver – still looking for a new building
- St Paul – THS Insourcing – **07/21/25**

Completed sites

Portland OR:

- Ongoing Activities:
 - Restack:
 - Medford
 - Eugene

Boise ID:

- Upcoming Activities:
 - Insource THS
 - Complete 08/19/24
 - Officially an RPDC: 10/1/24

RPDC Update – Projects on Hold


Santa Clarita LA:

Royal Palm FL:

Oklahoma City OK:

RTH Initiative

- Current Hub Sites:
 - Atlanta GA / Seminole (Orlando)
 - NJ NDC / Philadelphia PA NDC
 - Denver CO
 - San Fran NDC
 - Memphis TN
 - West Valley (Phoenix) / AZ RPDC
 - Indianapolis IN
 - Charlotte NC
 - Dallas TX
 - LA NDC
 - Pennwood
 - Des Moines IA
 - Kansas City MO
- Potential Hubs:
 - Jacksonville, FL

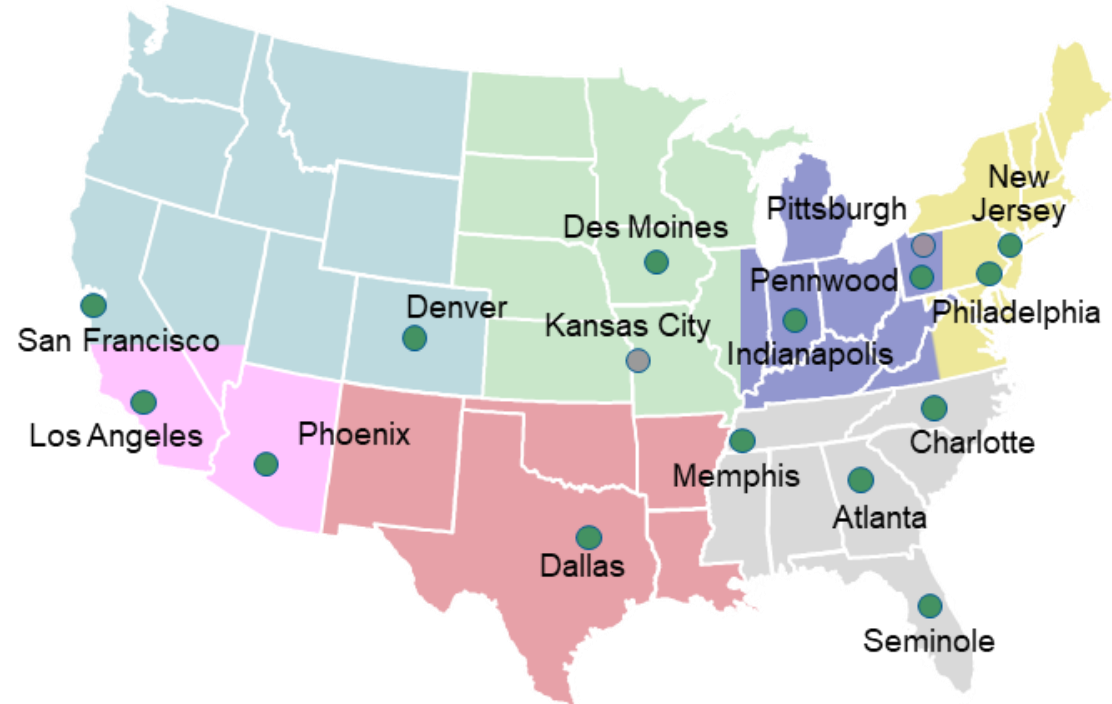

DFA Acronyms

- ❑ **RPDC:** Regional Processing & Distribution Center
- ❑ **LPC:** Local Processing Center
- ❑ **PSA:** Postal Support Annex
- ❑ **MaRS:** Matrix Regional Sorter
- ❑ **SIPS:** Single Induction Package Sorter
- ❑ **MEWS:** Matrix East West Sorter
- ❑ **MIMS:** Multiple Induct Matrix Sorter
- ❑ **HOPS:** High Output Package Sorter
- ❑ **CHOPS** – Chained HOPS
- ❑ **PILS:** Parallel Induction Linear Sorter
- ❑ **USS XL:** Universal Sort System handles larger packages
- ❑ **FRS:** Flexible Robotic System
- ❑ **LCUS:** Low Cost Universal Sorter: NMOs, trays, tubs
- ❑ **LCTS:** Low Cost Tray Sorter
- ❑ **HSTS:** High Speed Tray Sorter
- ❑ **RTH:** Regional Transfer Hub (Go East / Go West)
- ❑ **OTH:** Origin Transfer Hub
- ❑ **OPF:** Origin Processing Facility

Questions

Thank you
